


Coffs Harbour Boat Ramp Upgrade Stage 2
4 Week Lookahead – 1st September – 30th September 2023

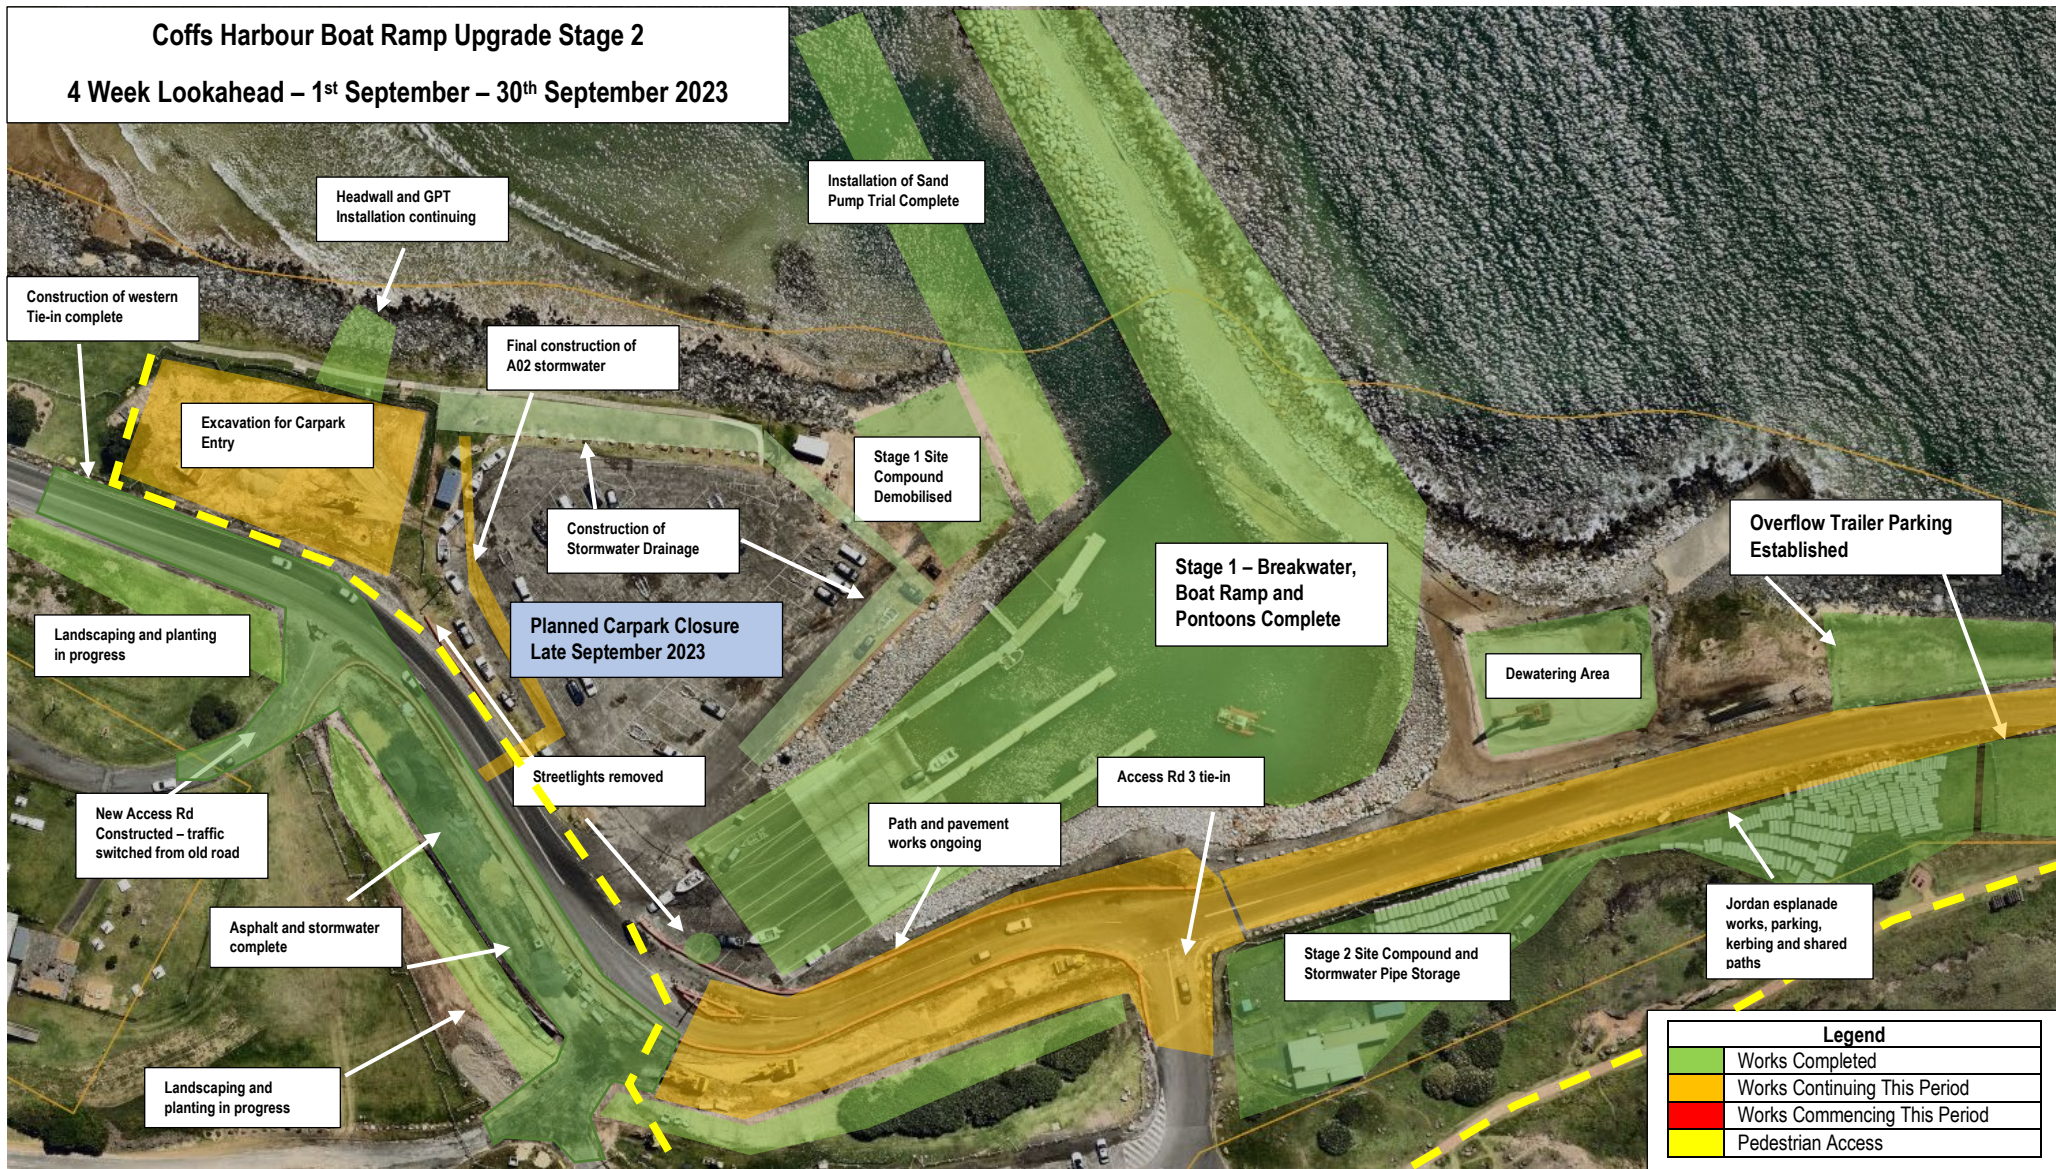

Headwall and GPT Installation continuing

Installation of Sand Pump Trial Complete

Construction of western Tie-in complete

Final construction of A02 stormwater

Excavation for Carpark Entry

Stage 1 Site Compound Demobilised

Construction of Stormwater Drainage

Stage 1 – Breakwater, Boat Ramp and Pontoons Complete

Overflow Trailer Parking Established

Landscaping and planting in progress

Planned Carpark Closure Late September 2023

Dewatering Area

Streetlights removed

Access Rd 3 tie-in

Path and pavement works ongoing

New Access Rd Constructed – traffic switched from old road

Asphalt and stormwater complete

Stage 2 Site Compound and Stormwater Pipe Storage

Jordan esplanade works, parking, kerbing and shared paths

Landscaping and planting in progress

Legend	
	Works Completed
	Works Continuing This Period
	Works Commencing This Period
	Pedestrian Access
