



Transport  
for NSW

# Transport Access Program

## Regional Station Upgrades

Market Sounding Livestream  
Information Session - Morning session

15 October 2020



# Acknowledgement of Country

Transport for NSW would like to acknowledge the traditional custodians and owners of the land in which we are all meeting today and pays that respect to Elders past, present and emerging and extends that respect to Aboriginal people who are joining us today.




# Agenda

1. Transport Access Program Overview
2. Indicative packaging strategy
3. Project scope
4. Drop in sessions
5. Market Sounding and Procurement Process
6. Next Steps
7. Q&A session



# How to ask a question

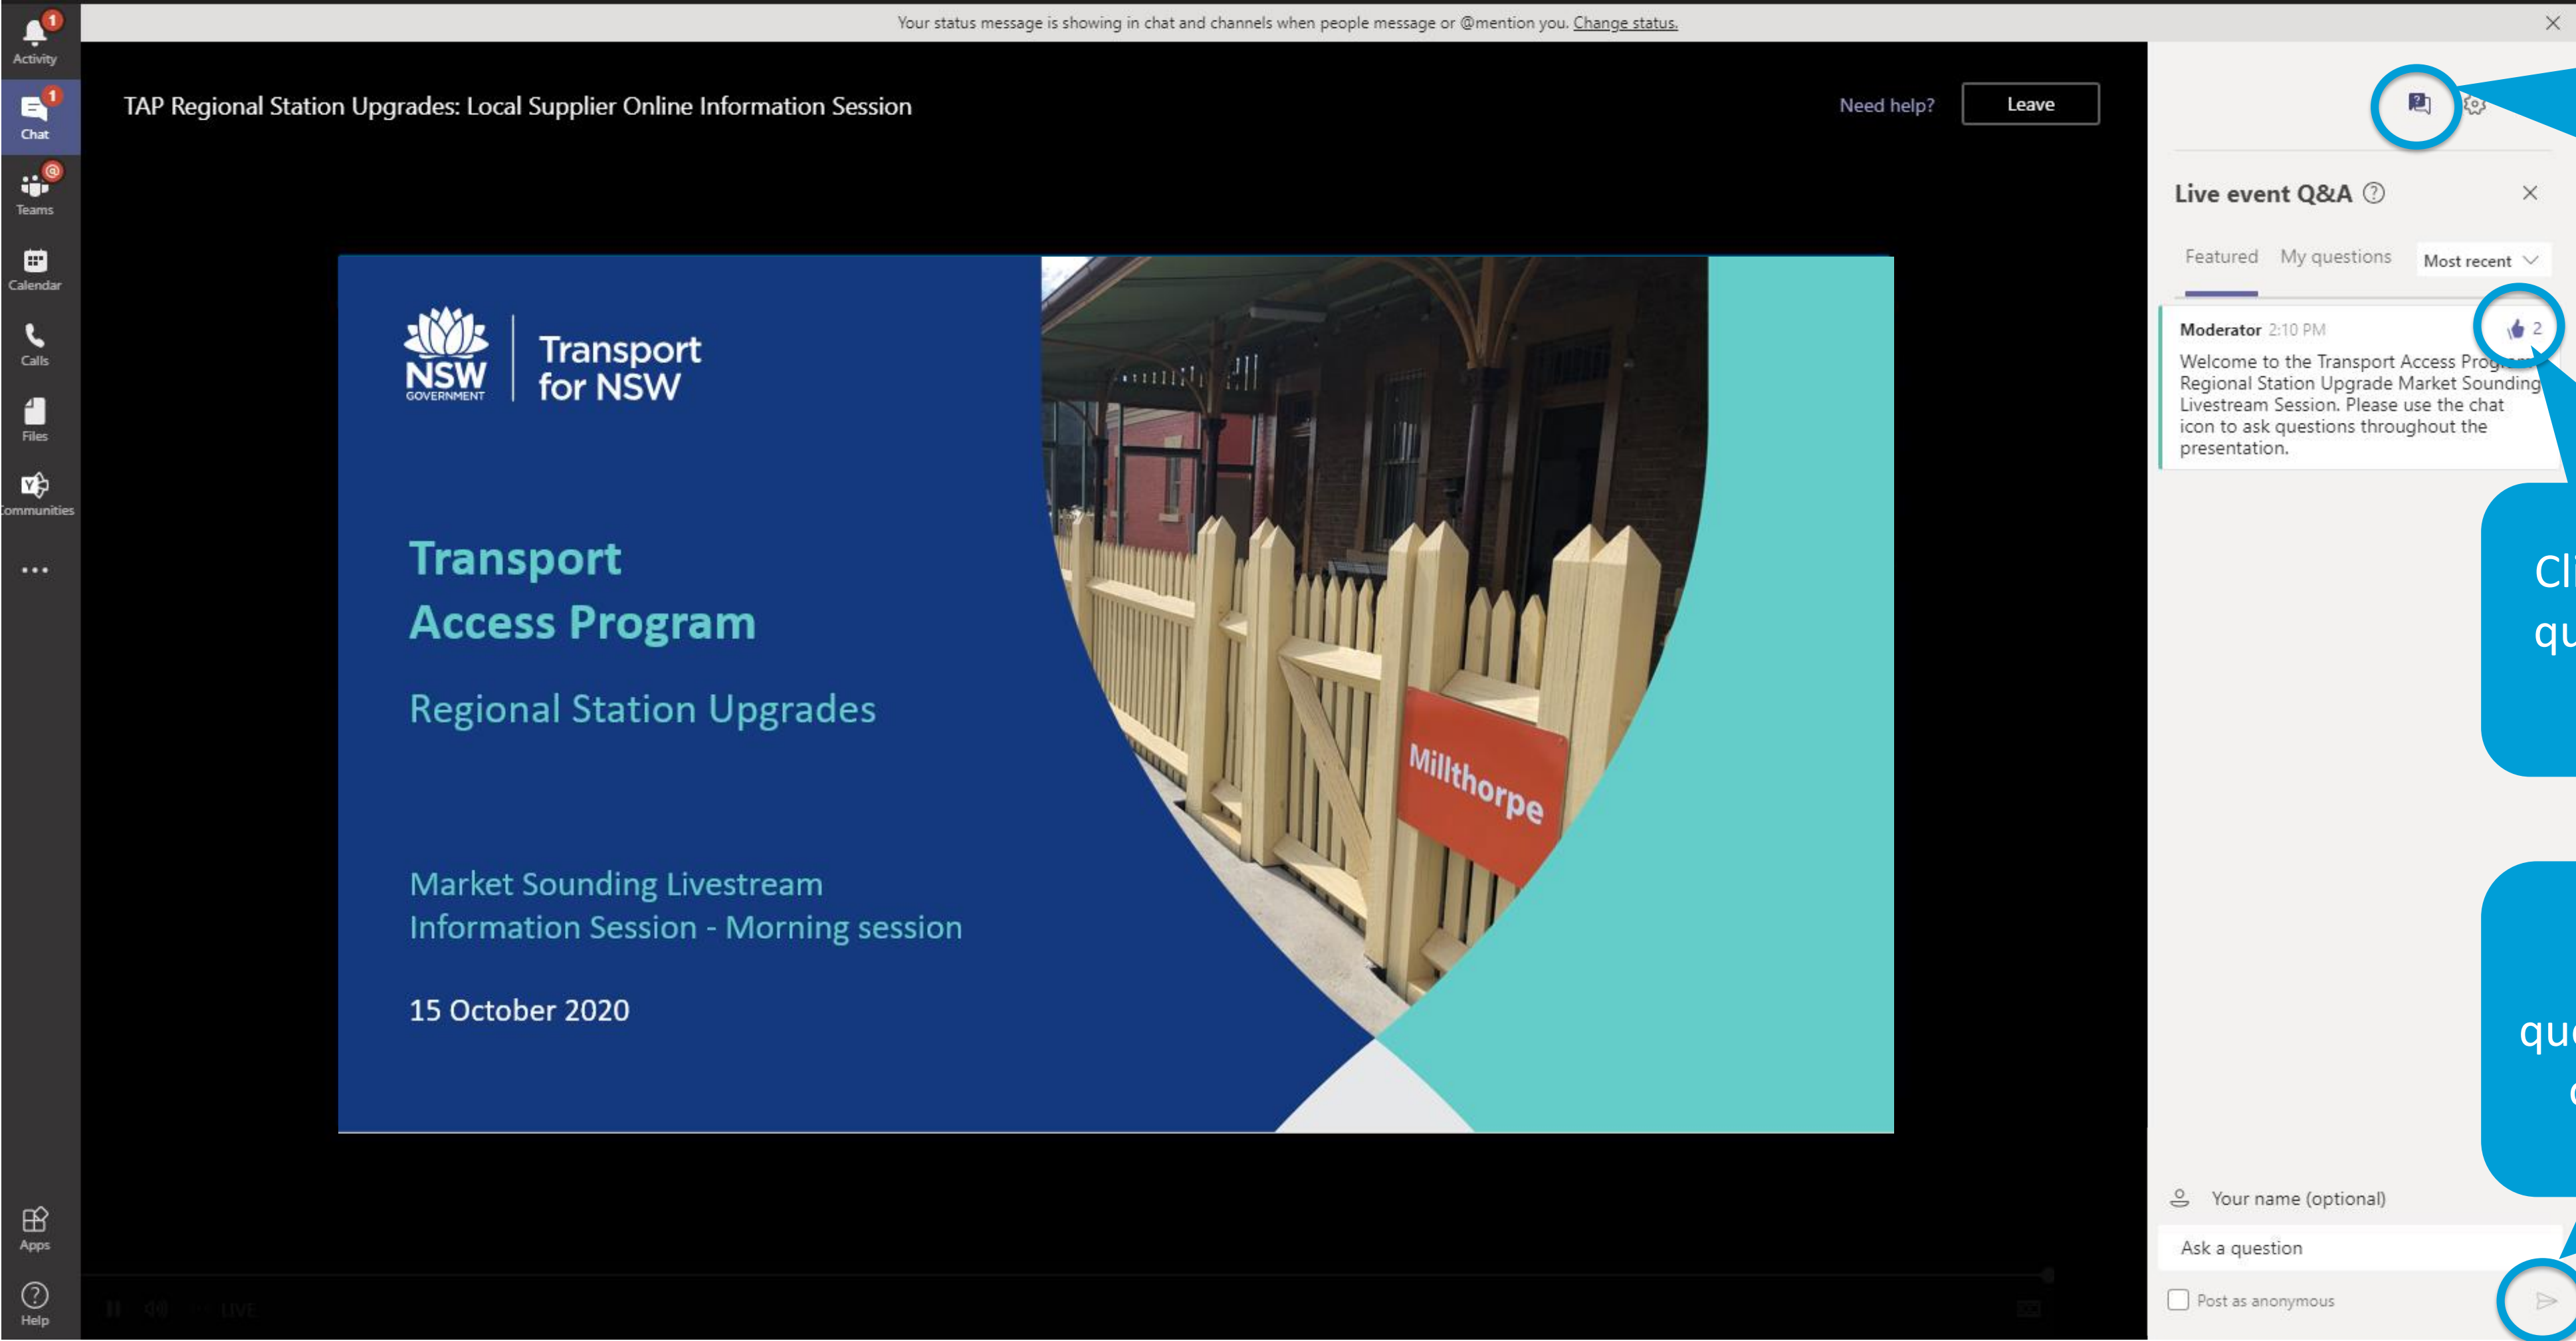


# Nadine Bourezg

Deputy Executive Director - Rail Delivery

# Transport Access Program

- Delivering accessible, modern, secure and integrated transport infrastructure.
- Improving access for all customers including the disabled, less mobile, parents/carers with prams and those using luggage.

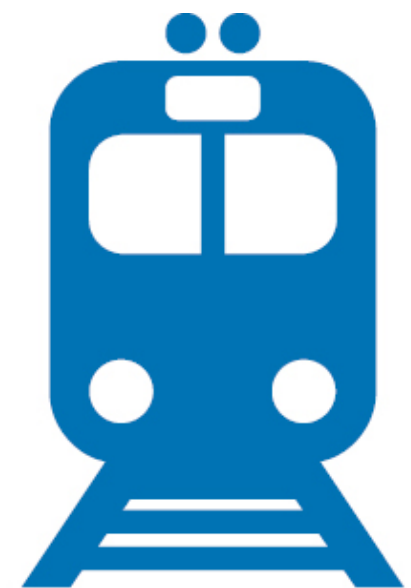

68 additional  
train station upgrades –  
**13 in regional NSW**



Station upgrades  
to achieve  
**DSAPT compliance**



**470+ projects**  
completed or  
underway




**\$885M over four years –**  
Total investment over \$2B

# Transport Access Program

Regional stations to be upgraded	
Armidale	Dubbo
Blayney	Griffith
Parkes	Moree
Wauchope	Grafton
Casino	Gunnedah
Narrabri	Taree
Queanbeyan	

**Orange** = Package 1 projects under construction and due for completion in 2020

**Blue** = Remaining projects with local business and supplier opportunities

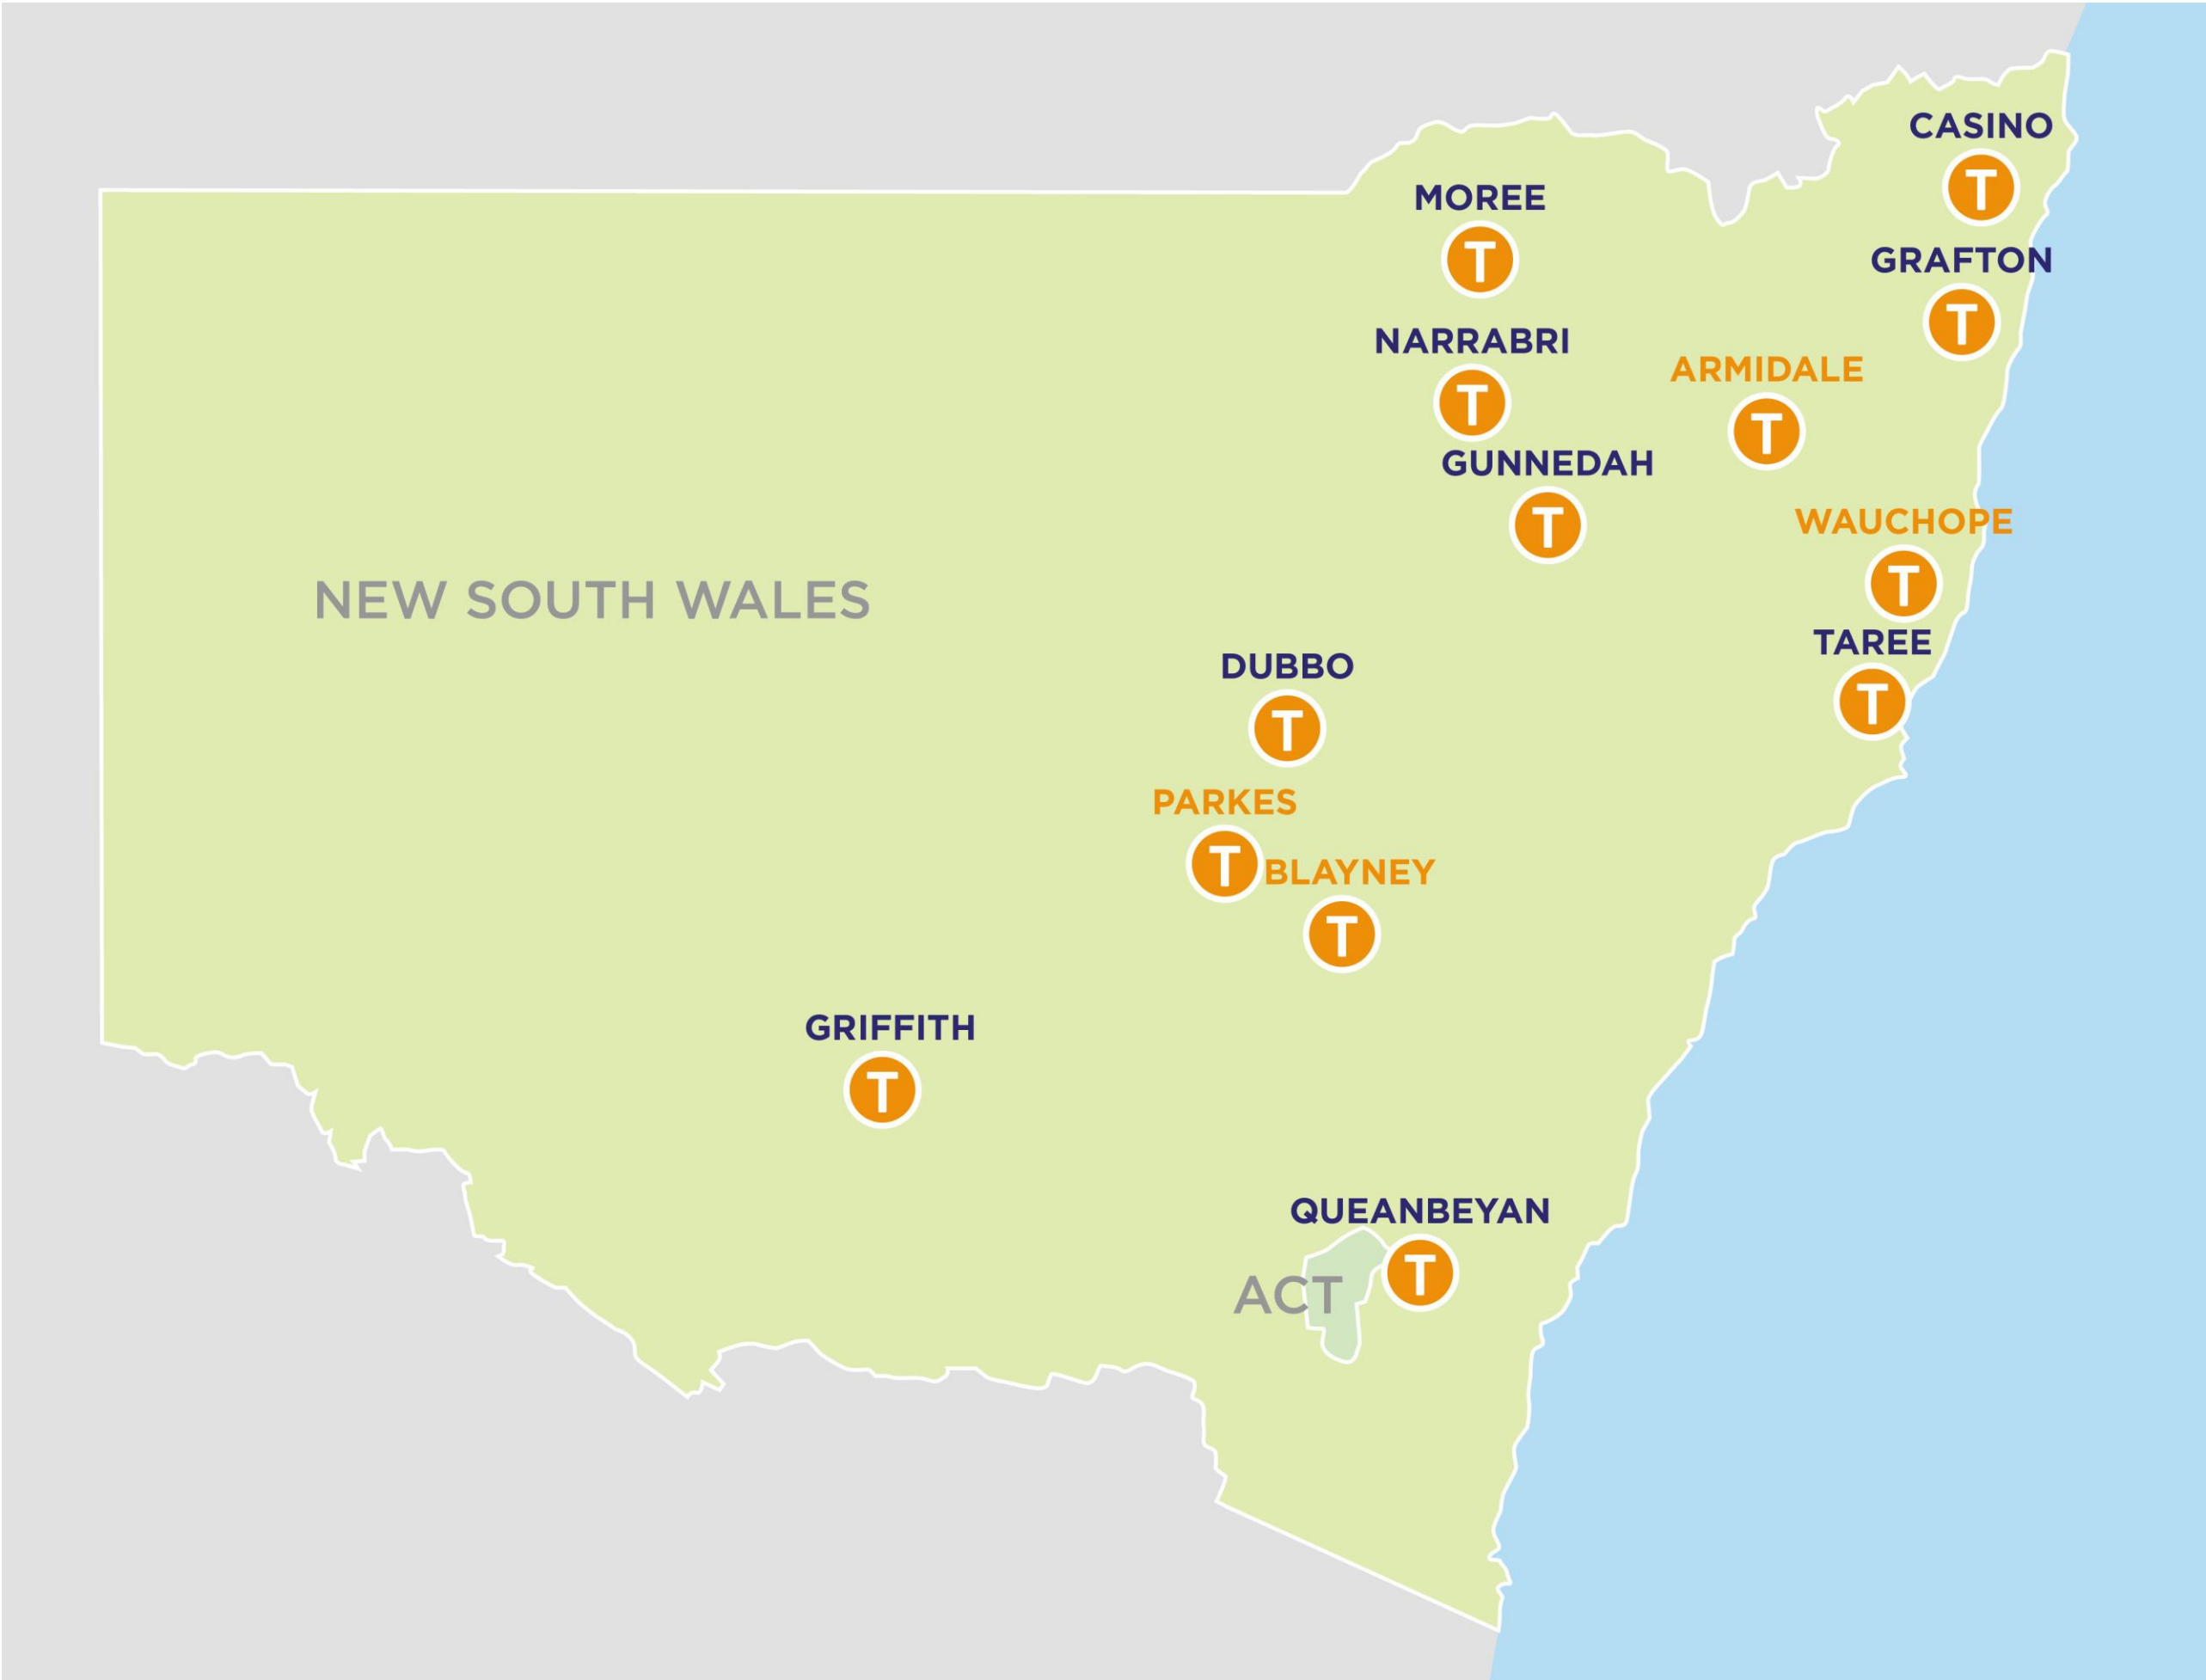

# Andrew Gay

## Senior Project Manager

# Regional Station Indicative Packaging Strategy

## PROPOSED CONTRACTING MIX

Station	Design	Construction
North West		
Moree		Construct Only
Narrabri		Construct Only
Gunnedah		
South & Central		
Dubbo	Design Only	Construct Only
Griffith	Design Only	Construct Only
Queanbeyan	Design Only	Construct Only
North Coast		
Casino	Design Only	Construct Only
Grafton		
Taree	Design Only	Construct Only

# Regional Station Upgrade Scope

Works *	Casino	Dubbo	Grafton	Griffith	Gunnedah	Moree	Narrabri	Queanbeyan	Taree
Upgrade DDA parking spaces & provide accessible pathway	✓	✓	✓	✓	✓	✓	✓	✓	✓
Platform upgrade works	✓	✓	✓	✓	✓	✓	✓		✓
Vehicle drop zone	✓	✓	✓		✓	✓		✓	✓
New ramps / stairs	✓		✓	✓	✓	✓	✓	✓	✓
Widened doors / auto openers	✓	✓	✓		✓			✓	✓
Track crossings						✓			
Accessible seating & waiting spaces	✓	✓	✓	✓	✓		✓	✓	✓
Upgrade ticket office counter	✓	✓	✓		✓			✓	✓
Male / female toilet works	✓	✓	✓	✓	✓		✓	✓	✓
Ambulant / family toilet works	✓	✓	✓	✓	✓		✓	✓	✓
Other accessible facilities	✓	✓	✓	✓	✓	✓	✓	✓	
Coach bay and / or bus boarding works				✓	✓	✓	✓		✓
* Scope is subject to detail design									

# Planning Approvals and Heritage

	State Heritage Register (SHR)	Section 170 Register
Casino	✓	
Dubbo	✓	
Grafton	✓	
Griffith		✓
Gunnedah	✓	
Moree		✓
Narrabri		✓
Queanbeyan	✓	
Taree	✓	

- Transport for NSW will undertake the planning and heritage approval process.
- All stations have heritage significance.
- Design inputs required to inform planning and heritage approval.
- Approvals are anticipated to be in place prior to construction commencement.

# Meet the project team

The project team will be holding a drop in session at each station in October and November to answer questions you have and discuss the scope of work.

Sunday 25 October	Monday 26 October	Tuesday 27 October	Wednesday 28 October	Thursday 29 October	Friday 30 October	Saturday 31 October
	Taree 10:30am – 12 noon	Casino 9:30am – 11:00am	Narrabri 9:15am – 10:45am	Dubbo 9:00am – 10:30am		
	Grafton 4:45pm – 6:15pm	Moree 4:30pm – 6:00pm	Gunnedah 1:00pm – 2:30pm			
Sunday 1 November	Monday 2 November	Tuesday 3 November	Wednesday 4 November	Thursday 5 November	Friday 6 November	Saturday 7 November
			Griffith 9:00am – 10:30am	Queanbeyan 9:00am – 10:30am		

# Eva Villaverde

## Senior Procurement Manager

# Market Sounding

- TfNSW will be issuing out a questionnaire for suppliers to complete as part of this market sounding
- The purpose of the market sounding is for Transport for NSW to:
  - provide an overview of the upcoming work and the scope of the packages across the regions
  - engage with as many relevant local businesses and suppliers as possible
  - understand local suppliers capabilities
  - learn more about interest levels of potential local suppliers to participate in the nine regional station upgrades
  - seek industry's feedback on the proposed contract packaging, extent of interest and capabilities of local contractors/suppliers.
- The market sounding process is expected to be completed by late November 2020.

# Market Sounding

- Transport for NSW will finalise the delivery and procurement strategies for the regional station upgrade packages following the market sounding process.
- This market sounding is **not** part of a formal procurement process and it is not a shortlisting process. Involvement (or not) in this market sounding will not affect or preclude any organisation's participation in any future procurement processes.
- Any future tendering processes will be advertised via the eTendering website. Suppliers are encouraged to register for eTendering to receive email notifications of upcoming tendering opportunities.

# Future Procurement Processes

- Pending completion of the market sounding and subsequent delivery and procurement strategies, indicative procurement timeframes are:
  - Release of initial tenders for North West Group – early to mid 2021
  - Release of initial tenders for South & Central Group – early to mid 2021
  - Release of initial tender for North Coast Group – early to mid 2021

## Recommended links:

[www.tenders.nsw.gov.au](http://www.tenders.nsw.gov.au) (NSW eTendering website) - for any NSW government tendering opportunities

[www.transport.nsw.gov.au/projects/current-projects/tap-3](http://www.transport.nsw.gov.au/projects/current-projects/tap-3) (further information and updates)

# Next Steps

- Market sounding questionnaire open for submission

Mid October  
2020

- Drop in sessions at station locations

October /  
November 2020

- Market sounding complete

Late November  
2020



# Q&A session

Nadine Bourezg

# How to ask a question

The screenshot shows a Microsoft Teams interface during a "TAP Regional Station Upgrades: Local Supplier Online Information Session". The main content area displays a "Q&A session" slide by "Nadine Bourezg". The slide footer includes "SENSITIVE: NSW GOVERNMENT" and the number "20".

On the right side, a "Live event Q&A" panel is visible. It features tabs for "Featured", "My questions", and "Most recent". A moderator message from 2:10 PM reads: "Welcome to the Transport Access Program Regional Station Upgrade Market Sounding Livestream Session. Please use the chat icon to ask questions throughout the presentation." Below this, there is a "thumbs up" icon with a count of "2".

At the bottom of the Q&A panel, there is a text input field labeled "Your name (optional)" and "Ask a question". Below this field is a checkbox for "Post as anonymous" and a "SEND" icon (a triangle inside a circle).

Three blue callout boxes provide instructions:

- Top callout: "Click this icon to show the Q&A function" (points to the Q&A icon in the top right corner of the Teams window).
- Middle callout: "Click 'thumbs up' for questions you would like answered" (points to the thumbs up icon in the Q&A panel).
- Bottom callout: "Type your name and question, and press 'ENTER' or click the 'SEND' icon" (points to the "SEND" icon at the bottom of the Q&A panel).

# Q&A session

Nadine Bourezg

# Still have questions

For more information or to speak with a member of the project team:



1800 684 490



projects@transport.nsw.gov.au



<https://www.transport.nsw.gov.au/projects/current-projects/tap-3>

# Thank you
